P1

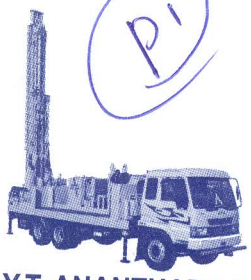

Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 1/6/18

No.

1. Customer's Name & Address : Benaka Developers and projects Ltd Bangalore.
2. Survey No. of Extent : Package No - 1 Ward No-6
3. Location : Saraji palya H P Govt school opp Temple
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 1/6/18
6. Depth of Borewell : 350 mts.
   a) Old Borewell : -
   b) New Borewell : ✓
7. Casing Pipe size and Depth : $6\frac{1}{2}$"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : 340 mts.
10. Water Yiled Obtained : 3"
11. Development of Borewell : 180, 265, 340 mts.
12. Static Water Level : 275 mts
13. Quality Water Level : Good
13. Cap & Collers : -

Beneficiary

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಟ್ಟದಾಸನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

T.D.O

SREE BORE WELLS
For Sree Borewells
Proprietor

For **SREE BOREWELLS**
Proprietor

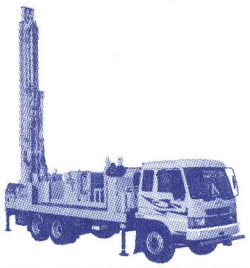

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 4/6/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd. Package No-1, Ward No-6
2. Survey No. of Extent :
3. Location : Sarayipalya. 2nd cross poojamantapa
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 4/6/18
6. Depth of Borewell : 385 mts
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : 190 mts
10. Water Yiled Obtained : 1.5 inch
11. Development of Borewell : 190, 280 mts
12. Static Water Level : 250 mts
13. Quality Water Level : Good & clear
13. Cap & Collers

Beneficiary

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ವಿದ್ಯಾರಣ್ಯಪುರ ಉಪ ವಿಭಾಗ

T.D.O.

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ವಿದ್ಯಾರಣ್ಯಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-24

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 6/6/18

No.

1. Customer's Name & Address : Benaka Developers & project ltd, Package No-I, Ward No-6
2. Survey No. of Extent :
3. Location : Sarayipalya opp Masjid road
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 6/6/18
6. Depth of Borewell : 60 mts
   a) Old Borewell : —
   b) New Borewell ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : Collapsed
10. Water Yiled Obtained : —
11. Development of Borewell : —
12. Static Water Level : —
13. Quality Water Level : —
13. Cap & Collers

Beneficiary ಬಿ.ಬಿ.ಎಂ.ಪಿ ಕುಡಿಯುವ ನೀರು ವಿಭಾಗ

T.D.O.

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor

ಬೆಂಗಳೂರು ಕಾರ್ಪೊರೇಷನ್ ಅಧಿಕಾರಿಗಳು
ಕುಡಿಯುವ ನೀರು ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 8/6/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd. Package No-1, Ward No-6
2. Survey No. of Extent :
3. Location : Sarayipalya. SR Layout Islamic School opp. Vidyasagar Govt school
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 8/6/18
6. Depth of Borewell : 350 mts
   a) Old Borewell : —
   b) New Borewell ✓ : 6½"
7. Casing Pipe size and Depth : —
8. Nature of Soil / Rocks etc. : Red Soil.
9. Water Srucked at : 160 mts
10. Water Yiled Obtained : 1½" inch
11. Development of Borewell : 160, 240, mts
12. Static Water Level : 200 mts
13. Quality Water Level : Good
13. Cap & Collers

Beneficiary

T.D.O.

For SREE BOREWELLS
SREE BORE WELLS
Proprietor



SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 12/6/18

No.

1.	Customer's Name & Address	:	Bonaka Developers & Projects Pvt Ltd. Package No-1 Ward No-6
2.	Survey No. of Extent	:	Sarayipalya Shabarinagar
3.	Location	:	2nd Main Road 2nd Cross
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	12/6/18
6.	Depth of Borewell	:	350 Feets
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	6½"
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	180 Feets
10.	Water Yiled Obtained	:	2" Inch
11.	Development of Borewell	:	Faild
12.	Static Water Level	:	-
13.	Quality Water Level	:	Good
13.	Cap & Collers		

Beneficiary

T.D.O.

For SREE BOREWELLS
Proprietor

SREE BORE WELLS

Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 13/6/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd. Package No- 1 Ward No-6
2. Survey No. of Extent : Shabari Nagar 3rd Main Road 3rd Cross
3. Location :
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 13/6/18
6. Depth of Borewell : 312 mts
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : 190 mts
10. Water Yiled Obtained : 2.5" Inch
11. Development of Borewell : 190, 280, 300 mts
12. Static Water Level : 220 mts
13. Quality Water Level : Good & Clear
13. Cap & Collers : —

Beneficiary

T.D.O.

SREE BORE WELLS
For SREE BOREWELLS
Proprietor



SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 15/6/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd
Package No-1 Ward No-6
2. Survey No. of Extent :
3. Location : Thanisandra, Arjunayatemple Road.
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 15/6/18
6. Depth of Borewell : 350 mts
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : 200 mts
10. Water Yiled Obtained : 2·75" Inch
11. Development of Borewell : 200, 250, 300 mts
12. Static Water Level : 160 mts
13. Quality Water Level : Good & clear
13. Cap & Collers

Beneficiary

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

T.D.O.

SREE BORE WELLS
For SREE BOREWELLS
Proprietor

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 5/7/18

No.

1. Customer's Name & Address : Renuka Developers & Projects ltd package no-1 ward no-6
2. Survey No. of Extent : Thanisandra. Arjunadri layout. Allalasandra road Near Masjid Road
3. Location :
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 5/7/18
6. Depth of Borewell : 350 mts
   a) Old Borewell : -
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : Faild
10. Water Yiled Obtained :
11. Development of Borewell : -
12. Static Water Level : -
13. Quality Water Level : -
13. Cap & Collers

Beneficiary

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

T.D.O.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

SREE BORE WELLS
For SREE BOREWELLS
Proprietor



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 6/7/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd. Package No-1 Ward No-6
2. Survey No. of Extent : Heggadevagala.
3. Location : BBMP office road.
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 6/7/18
6. Depth of Borewell : 350 mts
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red soil
9. Water Srucked at : 160 mts
10. Water Yiled Obtained : 3" inch
11. Development of Borewell : 160, 280, mts
12. Static Water Level : 160 mts
13. Quality Water Level : Good & clear
13. Cap & Collers

Beneficiary ಬಿ.ಬಿ.ಎಂ.ಪಿ. ವಿದ್ಯಾರಣ್ಯಪುರ ಉಪ ವಿಭಾಗ

T.D.O. ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ವಿದ್ಯಾರಣ್ಯಪುರ ಉಪ ವಿಭಾಗ ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

For SREE BOREWELLS
SREE BORE WELLS
Proprietor



SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date :...8/7/18.....

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd. Package No-1 Ward No-6
2. Survey No. of Extent :
3. Location : Thanisandra. Abbatt Nagar opp. George Public School
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 8/7/18
6. Depth of Borewell : 285 Feets
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil.
9. Water Srucked at : 125 Feets
10. Water Yiled Obtained : 35" Inch.
11. Development of Borewell : 125, 250 Feets
12. Static Water Level : 125 Feets
13. Quality Water Level : Good & clear
13. Cap & Collers : —

Beneficiary

T.D.O.

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 10/7/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd
Package No - 1
Ward No-6

2. Survey No. of Extent : Sarakki Jakya 2nd cross

3. Location : Main Outlet Layout
Raclenakalli

4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**

5. Drilling Date : 10/7/18

6. Depth of Borewell : 350 mts

a) Old Borewell : —

b) New Borewell : ✓

7. Casing Pipe size and Depth : 6 1/2"

8. Nature of Soil / Rocks etc. : Red Soil

9. Water Srucked at : 180 mts

10. Water Yiled Obtained : 2"

11. Development of Borewell : 180, 240 mts

12. Static Water Level : 150 mts

13. Quality Water Level : Good & clear

13. Cap & Collers : —

Beneficiary

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ವ್ಯಾಪಾರಯನುಮತಿ ಉಪ ವಿಭಾಗ

T.P.O.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ವ್ಯಾಪಾರಾನುಮತಿ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

SREE BORE WELLS
For SREE BOREWELLS
Proprietor



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 18/7/18

No.

1.	Customer's Name & Address	:	Benaka Developers & Projects Ltd Package No-1 Block No-6
2.	Survey No. of Extent	:	Sarayi Palya (Opp)
3.	Location	:	T.S Main Road (Thanisandra Road)
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	18/7/18
6.	Depth of Borewell	:	289 mts
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	$6\frac{1}{2}$"
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	165 mts
10.	Water Yiled Obtained	:	20 Litres/min.
11.	Development of Borewell	:	165, 260 mts
12.	Static Water Level	:	165 mts
13.	Quality Water Level	:	Good & clear
13.	Cap & Collers		

Beneficiary

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ವ್ಯಾಪಿರಾಯನಪುರ ಉಪ ವಿಭಾಗ

T.D.O.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ವ್ಯಾಪಿರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-28

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 23/7/18

No.

1.	Customer's Name & Address	:	Benaka Developers & Projects Ltd Package No-1 Ward No-6
2.	Survey No. of Extent	:	
3.	Location	:	Sarayipalya Maruthi Sevanagar Road Opp Tailor Shop.
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	23/7/18
6.	Depth of Borewell	:	350 mts
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	6½" 6mm
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	200 mts
10.	Water Yiled Obtained	:	2" inches
11.	Development of Borewell	:	200, 260 mts
12.	Static Water Level	:	200 mts
13.	Quality Water Level	:	Good & clear
13.	Cap & Collers		—

Beneficiary

T.D.O.

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor



SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 24/7/18

No.

1.	Customer's Name & Address	:	Renuka Developers & Projects Ltd Package No-1 Ward No-6
2.	Survey No. of Extent	:	Thanisandra, Nagavara Village, Byrathi Hobli
3.	Location	:	8th Cross Radhakrishnan Thanisandra 1200ft
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	24/7/18
6.	Depth of Borewell	:	350 mts
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	6½"
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	180 mts
10.	Water Yiled Obtained	:	2½ inch
11.	Development of Borewell	:	180, 250 mts
12.	Static Water Level	:	160 mts
13.	Quality Water Level	:	Good & clear
13.	Cap & Collers		—

Beneficiary

T.D.O.

For **SREE BOREWELLS**
Proprietor

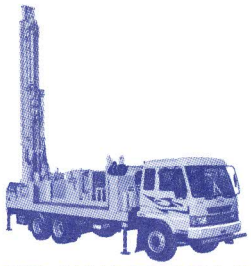

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

Y.T. ANANTHARAJU
Contractor

BOREWELL COMPLETION REPORT

Date : 4/9/18

No.

1.	Customer's Name & Address	:	Benaka Developers & Projects Ltd. Package No-1 Ward No-6
2.	Survey No. of Extent	:	Sawmill Road 7th Cross
3.	Location	:	Furniture Shop
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	4/9/18
6.	Depth of Borewell	:	350 Mts
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	6½"
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	220 Mts
10.	Water Yiled Obtained	:	350 Mts
11.	Development of Borewell	:	220 - 260 Mts
12.	Static Water Level	:	160 Mts
13.	Quality Water Level	:	Good & clear
13.	Cap & Collers		—

Beneficiary

T.D.O.

SREE BOREWELLS
For **SREE BOREWELLS**
Proprietor

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಧಿಕಾರಿಯವರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24



Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date : 7/9/18

No.

1.	Customer's Name & Address	:	Benaka Developers & Projects Ltd Package No - 1 Ward No.-6
2.	Survey No. of Extent	:	
3.	Location	:	Heggadevanagara 7th cross
4.	Drilling Unit Name	:	**SREE BOREWELLS, Vidyaranyapura, Bangalore**
5.	Drilling Date	:	7/9/18
6.	Depth of Borewell	:	350 mts
	a) Old Borewell	:	—
	b) New Borewell		✓
7.	Casing Pipe size and Depth	:	6½"
8.	Nature of Soil / Rocks etc.	:	Red Soil
9.	Water Srucked at	:	150 mts
10.	Water Yiled Obtained	:	2" inch.
11.	Development of Borewell	:	150, 280 mts
12.	Static Water Level	:	150 mts
13.	Quality Water Level	:	Good & clear
13.	Cap & Collers		—

Beneficiary

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

T.D.O.

SREE BORE WELLS

For **SREE BOREWELLS**
Proprietor

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

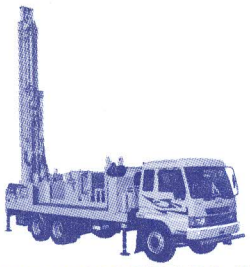

Y.T. ANANTHARAJU
Contractor

SREE BOREWELLS

Mobile : 9448257390
9916691295

6 1/2 & "BOREWELL DRILLERS
No. 110, Janani Apartment, G-1, Defence Layout, 4th Main,
Vidyaranyapura, Bangalore-97

BOREWELL COMPLETION REPORT

Date 27/7/18

No.

1. Customer's Name & Address : Benaka Developers & Projects Ltd.
   Package No-1
   Ward No-6
2. Survey No. of Extent : Kadlemahalli Village opp° Ganesha temple.
3. Location :
4. Drilling Unit Name : **SREE BOREWELLS, Vidyaranyapura, Bangalore**
5. Drilling Date : 27/7/18
6. Depth of Borewell : 350 mts
   a) Old Borewell : —
   b) New Borewell : ✓
7. Casing Pipe size and Depth : 6½"
8. Nature of Soil / Rocks etc. : Red Soil
9. Water Srucked at : 220 mts
10. Water Yiled Obtained : 1" inch.
11. Development of Borewell : 220-280 mts
12. Static Water Level : @ 160 mts
13. Quality Water Level : Good & clear
13. Cap & Collers : —

Beneficiary

T.D.O.

SREE BORE WELLS
For **SREE BOREWELLS**
Proprietor
